



Weekly Stakeholder Snapshot



Location: Sevenoaks Greatness Park
Project: Greatness Pavilion
Client: Sevenoaks Town Council / FC
Project Number: LG - 2395
Report Date: 31/07/2026
Week Number - 040



Patrick Steppel
Project Manager



On-site KPIs:

	Applicable	Comments
Health & Safety inspections completed	Yes	No health and safety issues to report
Programme reviewed	Yes	The programme has been reviewed, and we are currently on programme
Internal quality inspection undertaken	Yes	Not relevant to works on site, Currently.

Weekly Progress to Report:

This week has seen further significant progress across the works programme.

The groundworks team have completed installation of the road and path leading to the new Pavilion, with hoggin now laid and topsoil dressing applied to areas designated for reinstatement as grass; works have also commenced on the new bike path adjacent to the car park.

On the first floor, light fittings and PIR sensors have been installed, and the decorating team have completed all painting to this level.

Elsewhere, the metalwork team have amended the existing car park fencing to accommodate cyclist access to the new cycle lane and have finalised installation of the handrail to the external staircase.

The flooring team have completed installation of vinyl floor covering throughout the first floor.

From a procurement perspective we have placed orders with our mastic man and cleaners team as we approach the end of our programmed works.





Weekly Look Ahead:

Next week, our specialist green wall contractor will arrive on site to begin installation. The flooring team will finalise the remaining sections of vinyl flooring before progressing to floor carpet tile installation. The electrical team will fit lighting to the external areas and ground floor, while our decorators complete painting of all doors and frames throughout the ground floor. The mechanical team will carry out system testing, and the groundworks team will continue works on the new bike lane, with completion targeted for next week.

Early warnings and noticeable delays to the programme: No early warnings to report on site

Weekly Progress Photos:

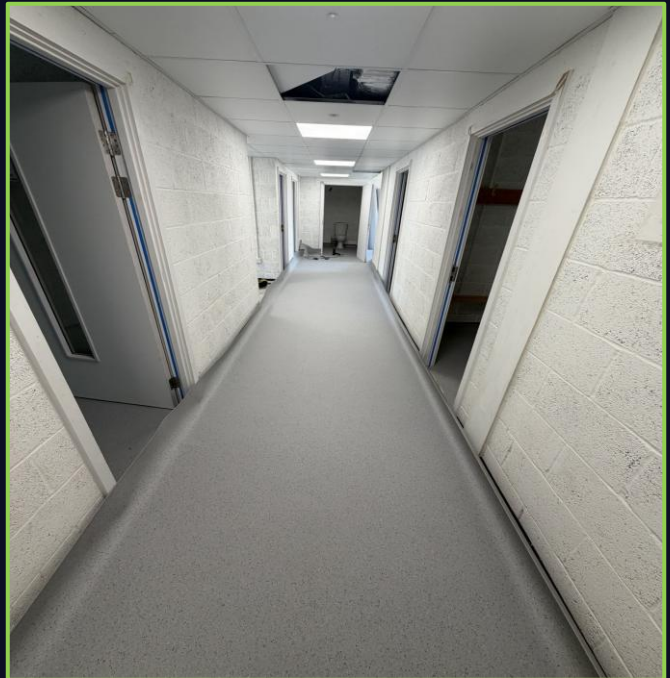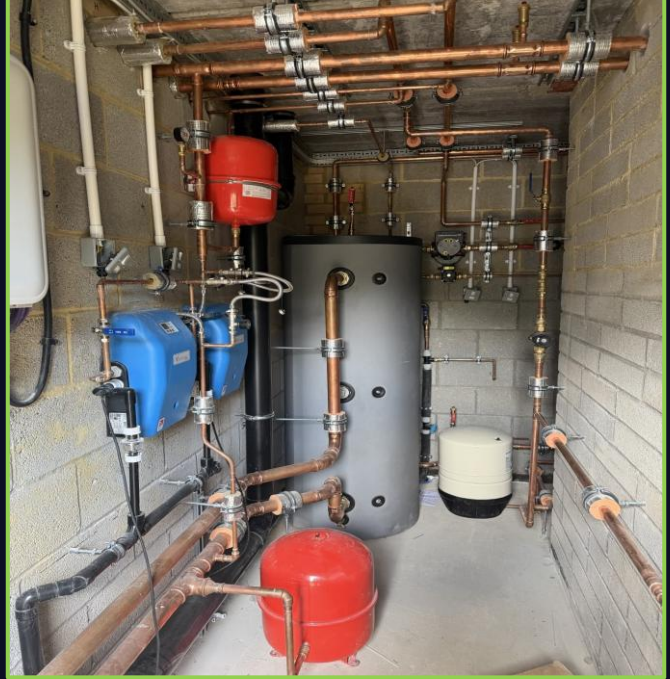

Social Values Highlights

Making a positive impact in our communities

SCHOOL ENGAGEMENT

30 pupils from St John's Primary School

- Pavilion site tour at Sevenoaks Town FC
- Construction process explained
- Interactive Q&A session



SUPPORTING LITERACY

Seven Kings School

- Books donated following project completion
- Titles selected by school librarian
- Supporting pupil reading development



COMMUNITY INCLUSION

Disability Festival in the Park

- Accessibility measures supported
- BSL interpreters and sensory spaces funded
- Free access maintained for attendees



GREEN CAREERS

Ilford County High School

- Year 7 sustainability workshop
- Career pathways in construction
- Green Building Challenge delivered

