



## Weekly Stakeholder Snapshot



Location: Sevenoaks Greatness Park  
Project: Greatness Pavilion  
Client: Sevenoaks Town Council / FC  
Project Number: LG - 2395  
Report Date: 14/08/2026  
Week Number - 042



Patrick Steppel  
Project Manager

On-site KPIs:

|                                        | Applicable | Comments                                                           |
|----------------------------------------|------------|--------------------------------------------------------------------|
| Health & Safety inspections completed  | Yes        | No health and safety issues to report                              |
| Programme reviewed                     | Yes        | The programme has been reviewed, and we are currently on programme |
| Internal quality inspection undertaken | Yes        | Not relevant to works on site, Currently.                          |

Weekly Progress to Report:

This has been a particularly productive week on site, with significant progress made across several work packages. Our groundworks team have made excellent progress this week, completing 95% of the car park hoggin, knee rail and bike lane installations. Work on the topsoil dressing is now 70% complete, with the remaining areas scheduled for completion in the coming week. We are pleased to confirm that our painting team have now completed all their work on site. Our electrical and mechanical teams have also completed their respective works and are now off site. Our floor layers have completed their final work on the internal staircase, while our roofing team have completed installation of the waterproof liquid system to the external staircase. Our green wall contractors have made good progress with the installation this week. The irrigation system has now been installed, along with the external frame and planting system, and the area is ready for the next phase of works, which will commence next week. All windows, both internally and externally, have received a professional clean this week. In addition, we have completed a full post-build sparkle clean throughout the property, with our mastic contractor completing the installation of silicone to all internal joints as required.




Weekly Look Ahead:

Looking ahead to next week, our groundworks team will conclude their works in the car park, along with general landscaping across the site. Our carpenter is booked in to fit the double handrail to the internal staircase and install door signage. The green wall contractors will test and commission the irrigation system on Monday, before moving on to the planting phase of their work, which is due to conclude by the end of next week. Once these works are complete, this will close out all outstanding works on the project.

**Early warnings and noticeable delays to the programme:** No early warnings to report on site




## Weekly Progress Photos:

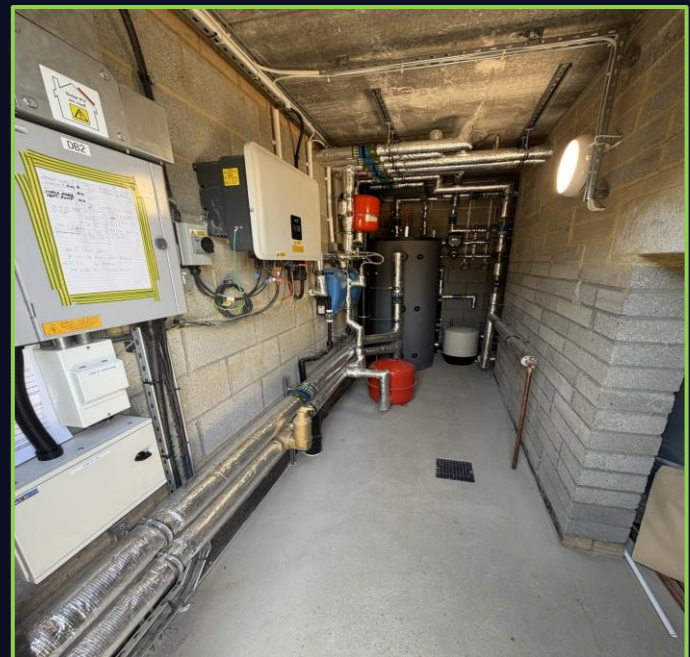



## Weekly Progress Photos:

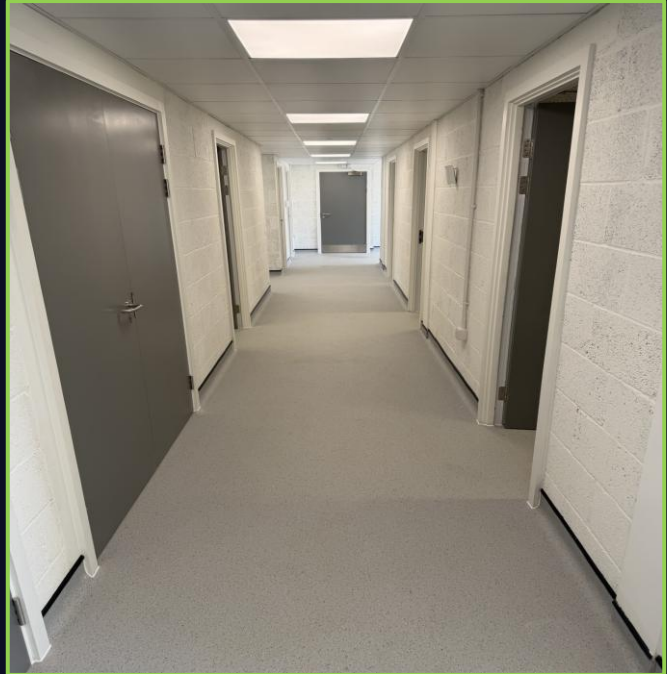

# Social Values Highlights

Making a positive impact in our communities

## SCHOOL ENGAGEMENT

30 pupils from St John's Primary School

- Pavilion site tour at Sevenoaks Town FC
- Construction process explained
- Interactive Q&A session



## SUPPORTING LITERACY

Seven Kings School

- Books donated following project completion
- Titles selected by school librarian
- Supporting pupil reading development



## COMMUNITY INCLUSION

Disability Festival in the Park

- Accessibility measures supported
- BSL interpreters and sensory spaces funded
- Free access maintained for attendees



## GREEN CAREERS

Ilford County High School

- Year 7 sustainability workshop
- Career pathways in construction
- Green Building Challenge delivered

